



Possible slides for IKON...

High level schedule – access for Instruments

1. Buildings are NOT delayed !

*Hall access for Instruments according to baseline schedule – plan to start installations outside Bunker area as soon as you get access. First installation (and binder!) takes time.
Cranes are confirmed to be available from point of instrument access.*

2. Target delayed -> impacting in-bunker access

Identifying mitigations to minimise the delays to the extent possible

Important that we get real forecasts from Instruments, so that we don't implement mitigations in areas where instruments aren't ready for installation. When are instruments ready?



Target delays

Impacting NSS

Vessel, inner shielding, portblocks etc – all need to be installed before the insert installations can start. These WP have delays, deliveries are foreseen Q4-20 / Q1-21.

<i>Light shutter system</i>	<i>forecasted deliveries Q2-Q3 2021</i>
<i>Blindplugs</i>	<i>confirmed deliveries Q4202-Q1 2021</i>
<i>NBPI</i>	<i>forecasted deliveries between June-21 and Feb-22</i>

NSS

<i>NBOA</i>	<i>deliveries Q42020 – Q22021, not pushing Insert installations</i>
-------------	---

Inserts (NBOA&NBPI or blindplugs), Light shutters, NBW etc needs to be installed before the instruments can start their in-bunker access.

In bunker access – status as of August 2020


based on today's plan (rolling wave schedule)

Section 1 = NORTH	start Sep 2021
Section 2 = SOUTH	start Oct 2021
Section 3 = EAST	start Nov 2021
Section 4 = WEST	start March 2022

(status TD rolling wave plan 31 Aug 2020)






Section 1 = NORTH	LOKI, TBL, FREIA
Section 2 = SOUTH	ODIN, DREAM
Section 3 = EAST	ESTIA, SKADI, VESPA
Section 4 = WEST	CSPEC, BIFROST, MAGIC, BEER, NMX, TREX, MIRACLES, HEIMDAL

BOLD = First 8

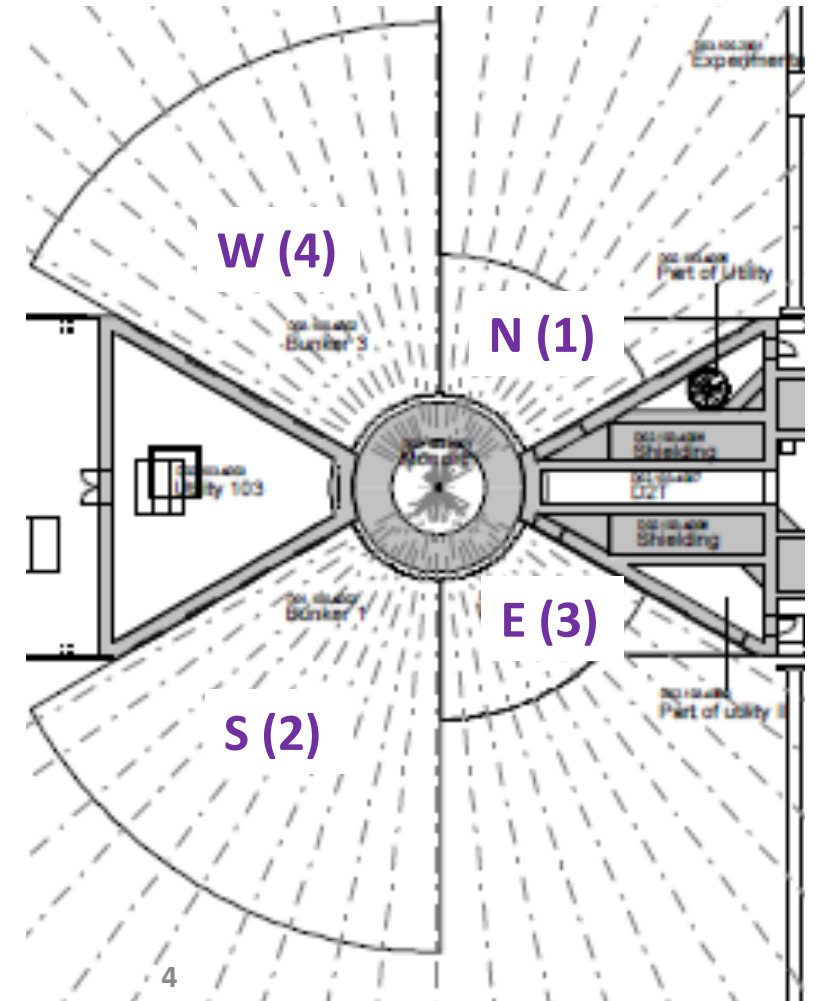

Components in-bunker

West

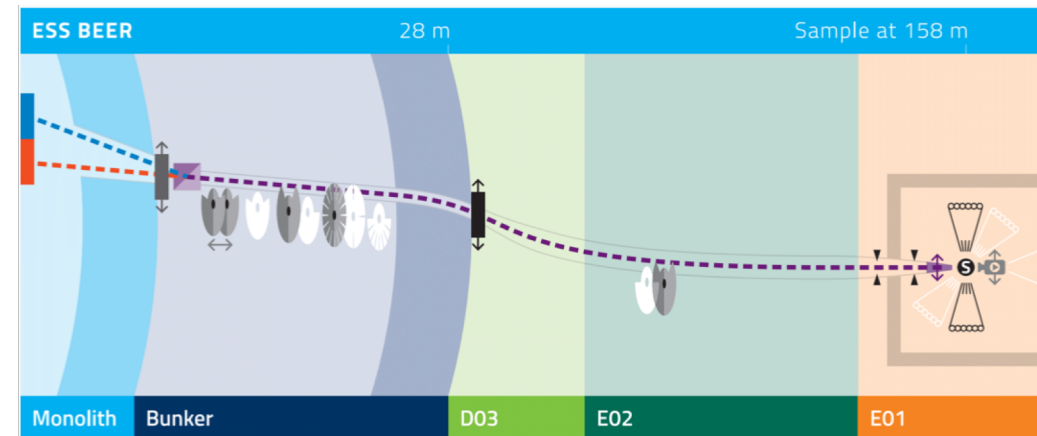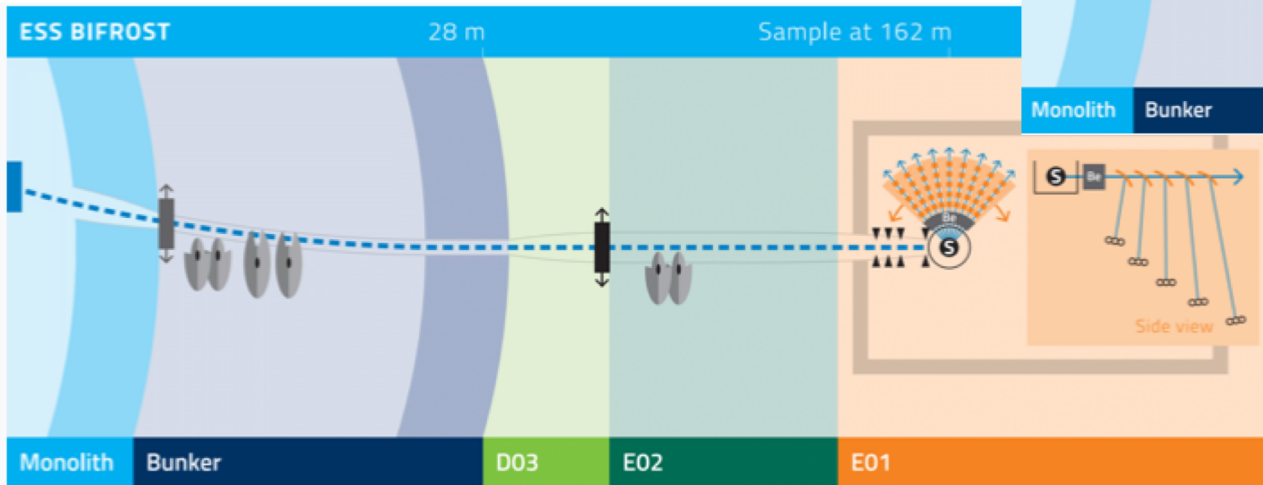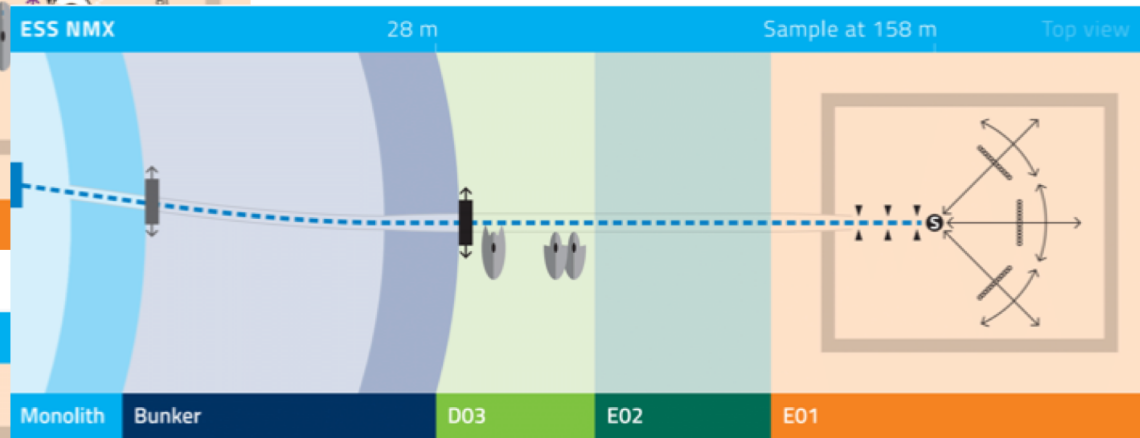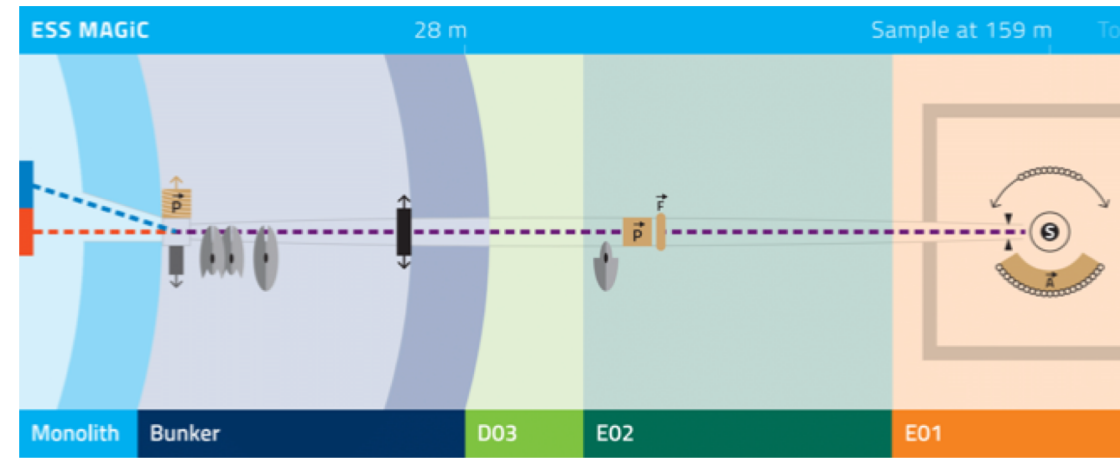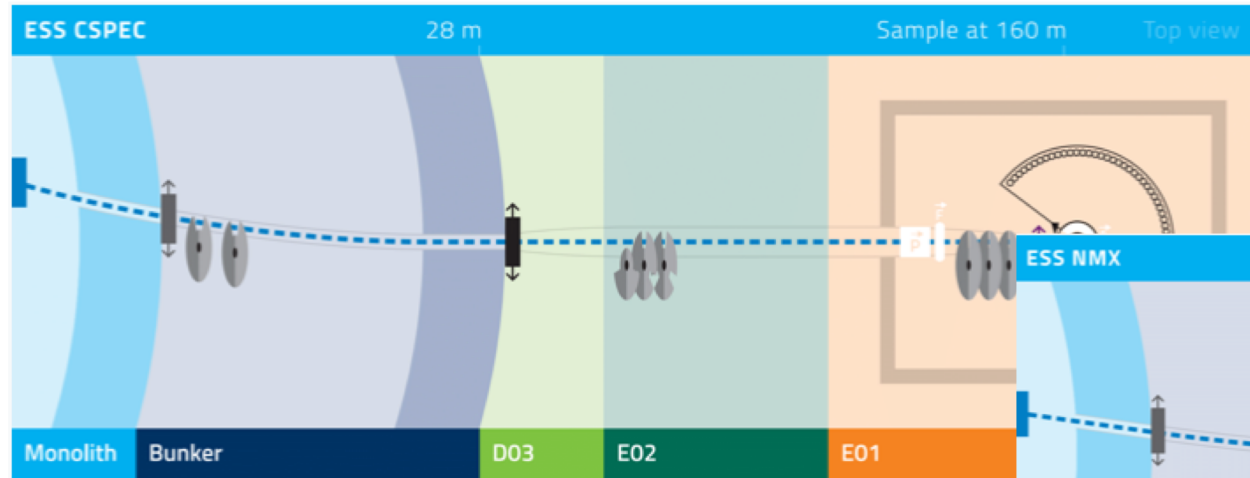

Components in-bunker

North, South & East

