


Project: 5EC8IPS01_20210302
Date: mié 10/03/21

Tarea Progreso Resumen Tareas externas Fecha límite
 División Hito Resumen del proyecto Hito externo

Id	Nombre de tarea	Port	Duración	Comienzo	Fin	03 may '21	10 may '21	17 may '21	24 may '21	31 may '21	07 jun '21	14 jun '21	21 jun '21	28 jun '21	05 jul '21	12 jul '21	19 jul '21	26 jul '21	02 ago '21	09 ago '21			
						S	D	L	M	X	J	V	S	D	L	M	X	J	V	S	D	L	M
48	Welding of Port Tube #10	N2	2 días	jue 24/06/21	lun 28/06/21																		
49	Welding of Port Tube #11	E7	2 días	jue 24/06/21	lun 28/06/21																		
50	Welding of Port Tube #12	S3	2 días	jue 24/06/21	lun 28/06/21																		
51	Welding of Port Tube #13	W4	2 días	lun 28/06/21	mié 30/06/21																		
52	Welding of Port Tube #14	E3	2 días	lun 28/06/21	mié 30/06/21																		
53	Welding of Port Tube #15	S7	2 días	lun 28/06/21	mié 30/06/21																		
54	Welding of NN-Bar	NNBar	3,5 días	mié 30/06/21	mar 06/07/21																		
55	NDT NN-Bar + Port Tubes		7,5 días	mar 29/06/21	vie 09/07/21																		
56	NDTs NN-Bar	NNBar	1 día	mar 06/07/21	mié 07/07/21																		
57	NDTs Port Tubes #1-15		7,5 días	mar 29/06/21	vie 09/07/21																		
58	6 Port Tube Tack welding + BGS (Backing gas system) intallation		6 días	mié 07/07/21	jue 15/07/21																		
59	Tack weld & BGS of Port Tube #34	W9	1 día	mié 07/07/21	jue 08/07/21																		
60	Tack weld & BGS of Port Tube #35	N7	1 día	jue 08/07/21	vie 09/07/21																		
61	Tack weld & BGS of Port Tube #36	N9	1 día	vie 09/07/21	lun 12/07/21																		
62	Tack weld & BGS of Port Tube #37	W7	1 día	lun 12/07/21	mar 13/07/21																		
63	Tack weld & BGS of Port Tube #38	W8	1 día	mar 13/07/21	mié 14/07/21																		
64	Tack weld & BGS of Port Tube #39	N8	1 día	mié 14/07/21	jue 15/07/21																		
65	Complete welding of remaining Port Tubes		19,5 días	mié 30/06/21	mié 28/07/21																		
66	Welding of Port Tube #16	W1	2 días	mié 30/06/21	vie 02/07/21																		
67	Welding of Port Tube #17	N4	2 días	mié 30/06/21	vie 02/07/21																		
68	Welding of Port Tube #18	S11	2 días	vie 02/07/21	mar 06/07/21																		
69	Welding of Port Tube #19	W9	2 días	jue 08/07/21	lun 12/07/21																		
70	Welding of Port Tube #20	N5	2 días	mié 07/07/21	vie 09/07/21																		
71	Welding of Port Tube #21	E10	2 días	mar 06/07/21	jue 08/07/21																		
72	Welding of Port Tube #22	N1	2 días	lun 12/07/21	mié 14/07/21																		
73	Welding of Port Tube #23	S10	2 días	vie 09/07/21	mar 13/07/21																		
74	Welding of Port Tube #24	N7	2 días	vie 09/07/21	mar 13/07/21																		
75	Welding of Port Tube #25	W7	2 días	mié 14/07/21	vie 16/07/21																		
76	Welding of Port Tube #26	S4	2 días	mar 13/07/21	jue 15/07/21																		
77	Welding of Port Tube #27	N9	2 días	mar 13/07/21	jue 15/07/21																		
78	Welding of Port Tube #28	W8	2 días	vie 16/07/21	mar 20/07/21																		
79	Welding of Port Tube #29	N3	2 días	jue 15/07/21	lun 19/07/21																		
80	Welding of Port Tube #30	S8	2 días	jue 15/07/21	lun 19/07/21																		
81	Welding of Port Tube #31	W3	2 días	mar 20/07/21	jue 22/07/21																		
82	Welding of Port Tube #32	E4	2 días	lun 19/07/21	mié 21/07/21																		
83	Welding of Port Tube #33	S2	2 días	lun 19/07/21	mié 21/07/21																		
84	Welding of Port Tube #34	W5	2 días	jue 22/07/21	lun 26/07/21																		
85	Welding of Port Tube #35	N8	2 días	mié 21/07/21	vie 23/07/21																		
86	Welding of Port Tube #36	E6	2 días	mié 21/07/21	vie 23/07/21																		
87	Welding of Port Tube #37	E2	2 días	lun 26/07/21	mié 28/07/21																		
88	Welding of Port Tube #38	S6	2 días	vie 23/07/21	mar 27/07/21																		
89	Welding of Port Tube #39	E8	2 días	vie 23/07/21	mar 27/07/21																		
90	NDT remaining Port Tubes		12 días	lun 12/07/21	mié 28/07/21																		
91	NDTs Port Tubes #16-39		12 días	lun 12/07/21	mié 28/07/21																		
92	Connection Pipe		2 días	mié 28/07/21	vie 30/07/21																		
93	Welding		1,5 días	mié 28/07/21	jue 29/07/21																		
94	NDTs		0,5 días	jue 29/07/21	vie 30/07/21																		

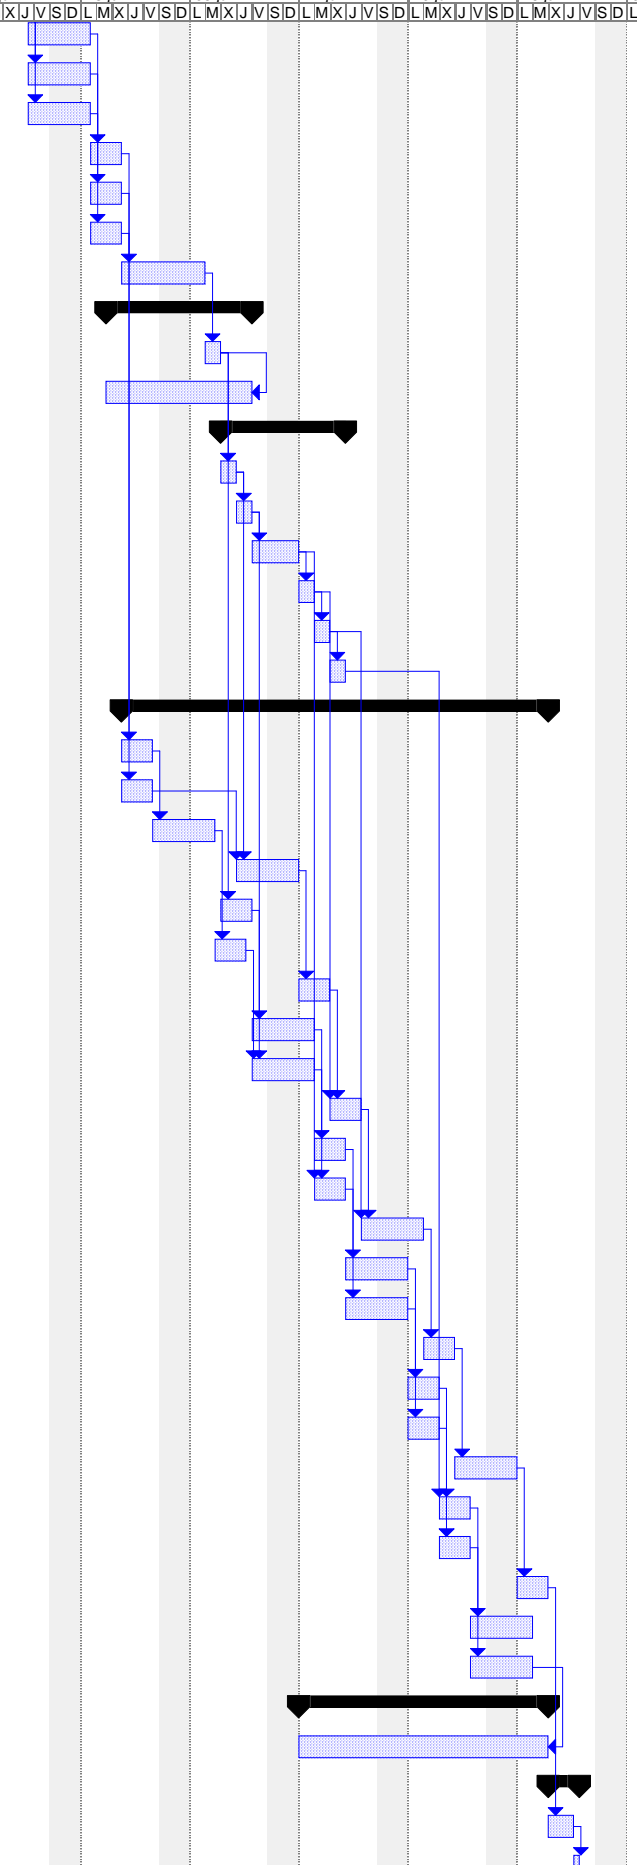

Project: 5EC8IPS01_20210302
Date: mié 10/03/21

Tarea: Progreso
División: Hito

Resumen: Resumen del proyecto
Tareas externas: Hito externo

Fecha límite:
